

COSTA PALMAS



Project Information:

Project Name: Cabana

Project Location: Los Cabos, BCS

100.- Organization

Costa Palmas Homes

Anselmo Saldaña Tyler Jorgenson Alonso Gonzalez Christelle García Ana Laura Tostado José Rueda Lorena Castillo Enrique Robles

PEC Team

Job Title Manager - CP Homes Design Director

Head of Construction Design Manager Designer

Construction Manager Design - CP Homes

Contruction

Job Title

Hanni Paz AOR Iván Parra AOR Osvaldo Estrada AOR Iván Nieves AOR Javier Marroquín AOR

PIZA Team Job Title

Jeimi Cuendulain BIM&TECH Manager Miriam Herrera BIM&TECH Administrator Manuel Curiel BIM&TECH Administrator Raúl Valadez Construction Manager Damian Pizá

Project Director

Mail

asaldana@costapalmas.com tjorgenson@irongp.com agonzalez@costapalmas.com chgarcia@costapalmas.com atostado@costapalmas.com jrueda@costapalmas.com lcastillo@costapalmas.com drobles@costapalmas.com

Mail


hpaz@estudiopec.com parra@estudiopec.com estrada@estudiopec.com inieves@estudiopec.com jmarroquin@estudiopec.com

jeimi.cuendulain@pizaconsulting.com miriam.herrera@pizaconsulting.com manuel.curiel@pizaconsulting.com raul.valadez@pizaconsulting.com

dp@pizaconsulting.com

200.- Comunication


Meeting Commitments (Minutes)



Responsable


Minutes

Total: 185




Point	Status	Responsable	Question
112	•		De acuerdo a la reunion del 25 de Agosto de VDC, JR comentó sobre la problemática de un tipo de geotextil que retiene sedimentos que ocasionan una mala filtración. Del mismo modo se pide detaller muy bien esta seccion, ya que en la reunion se hablo de geotextil alrededor de la tuberia, se hablo de utilizar una media caña, asi como de piedra decorativa y estancamiento de agua
117	•		Favor de proporcionar detalle de pluvial que cruza en zona de Zapata superficial, y confirmar que esta tuberfa hará el paso por la contratrabe, proporcionar detalle en plano.









300.- BIM Model

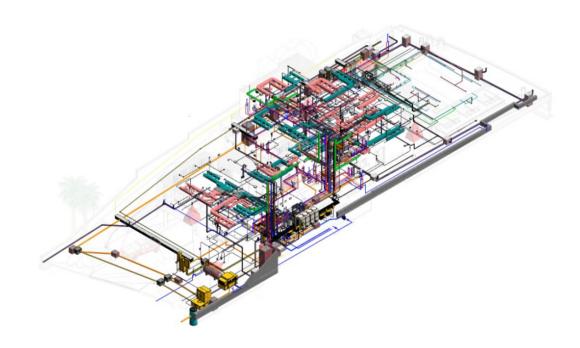

300.- Document Control



Received Drawings by Sub- Discipline



400.- Relevant Commitments

Primary	Status	Closed	Task Name Week 12th to 16th of October	Responsable
0.00		✓	PEC submitted three transmittals during this week with an update on Architectural, Structural and MEP Drawings.	Hanni Paz
0.00	•		PEC to give the following up to the ARFIs and BIM360 Issues on this next week. The status is: • Open: 275 • Answered: 256 • Close: 169 • Canceled: 12 • Urgent: 3 • Total: 715	Hanni Paz
0.00	•		PIZA to submit Level 3 OV20 Cabana of BIM Model	Jeimi Cuendulain
0.00	•		The site visit by Piza Team will be the following Wednesday, October 21rst.	Jeimi Cuendulain

500.- Project Progress

Activities 3WLA

Tarea	Status	Assigned To	Duration	Start	Finish	% Complete.	% Programmed	Dif	Oct 18 Oct 25 No
	Otatao	7.001g1104 10							F S S M T W T F S S M T W T F S S M T V
OV20, rev 3 (Agosto 27)			96d	26-Aug-2020	29-Nov-2020	64%	63%	1%	
NIVEL 3			20d	3-Oct-2020	22-Oct-2020	66%	62%	4%	NIVEL 3
ARQ. EST.	•	Jeimi Cuendulain	15d	3-Oct-2020	17-Oct-2020	95%	93%	2%	ARQ. EST.
MEP	•	Manuel Curiel	15d	3-Oct-2020	17-Oct-2020	95%	93%	2%	MEP
ESPECIALIDADES	•	Miriam Herrera	10d	12-Oct-2020	21-Oct-2020	60%	50%	10%	ESPECIALIDADES
REVISION FINAL	•	Jeimi Cuendulain	15d	8-Oct-2020	22-Oct-2020	65%	60%	5%	REVISIÓN FINAL
ARFI	•	Jeimi Cuendulain	15d	8-Oct-2020	22-Oct-2020	15%	10%	5%	ARFI
ENTREGAS	•		16d	23-Oct-2020	7-Nov-2020	0%	0%	0%	
Quantity Take offs	•	Jeimi Cuendulain	16d	23-Oct-2020	7-Nov-2020	0%	0%	0%	
Savings Reports	•	Jeimi Cuendulain	16d	23-Oct-2020	7-Nov-2020	0%	0%	0%	
RVT Submitted to CPH	•	Damian Piza	16d	23-Oct-2020	7-Nov-2020	0%	0%	0%	

Click to see the complete Schedule

CPH.AS_S_Curve

